



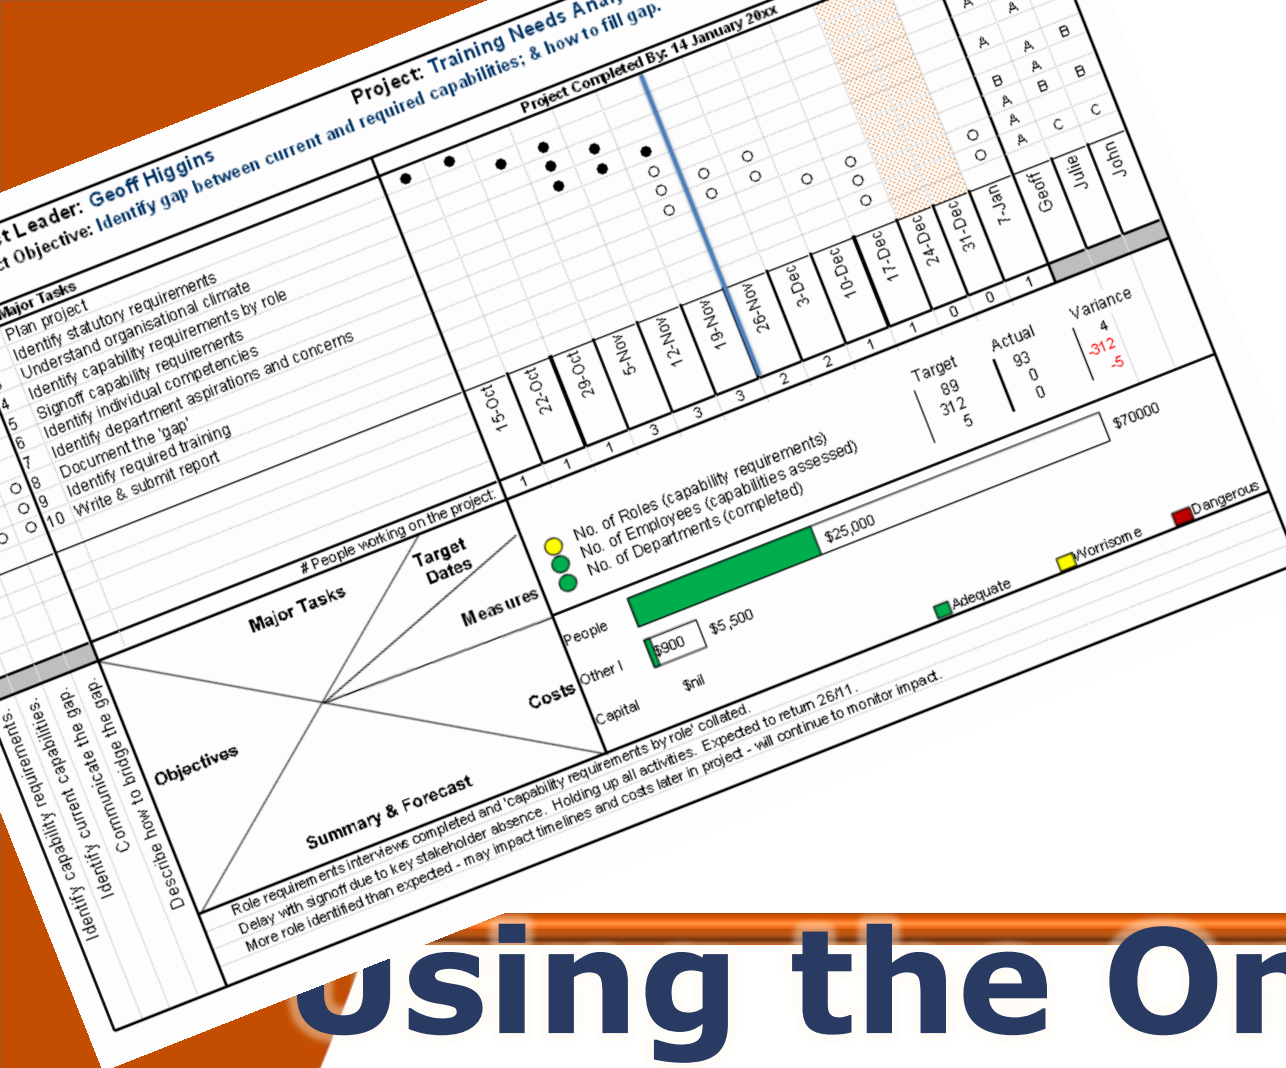

# Using the One Page Project Manager™

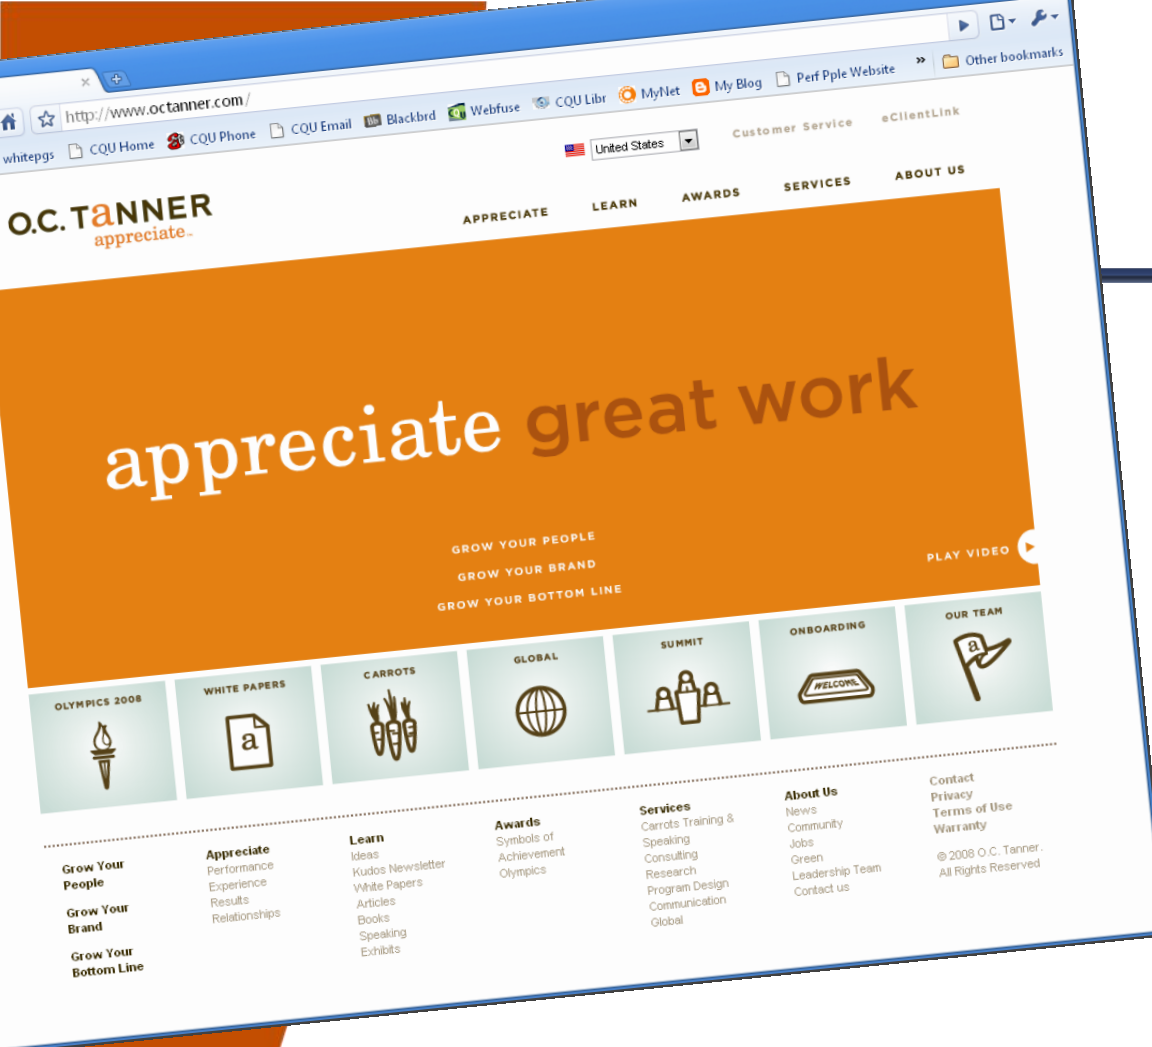

# Attribution(1)


The One Page Project Manager™ is the intellectual property of O.C. Tanner Company (USA).

# Attribution(2)

---

Clark Addison Campbell has published a book called *The One-Page Project Manager* (2007, John Wiley & Sons).

This was a key source of content in this presentation.

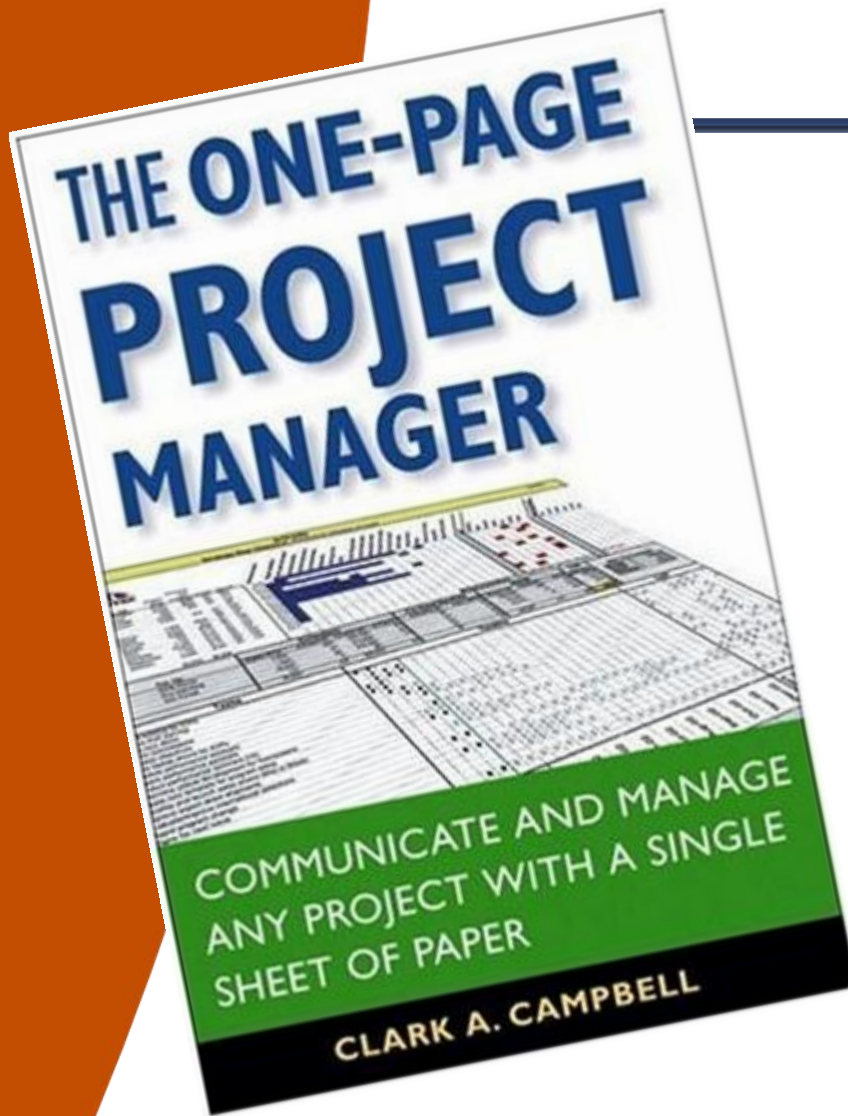



# Attribution(3)

The website of the *The One-Page Project Manager* book includes a resources page, with examples and the OPPM Template (for Excel).

This template was a key source of content in this presentation.

# Purpose

---

- To understand how the One Page Project Manager™ can be used as a tool for planning, monitoring and communicating project performance.
- To be able to develop a One Page Project Manager™ for your own project.



# Topics

---


- The One Page Project Manager™
- Planning
- Your Own Project
- Monitoring & Reporting
- Reading the OPPM

# Question

---



1. What is the core information that any person needs to know about your project...
  - a) ... before you start?
  - b) ... part way through?

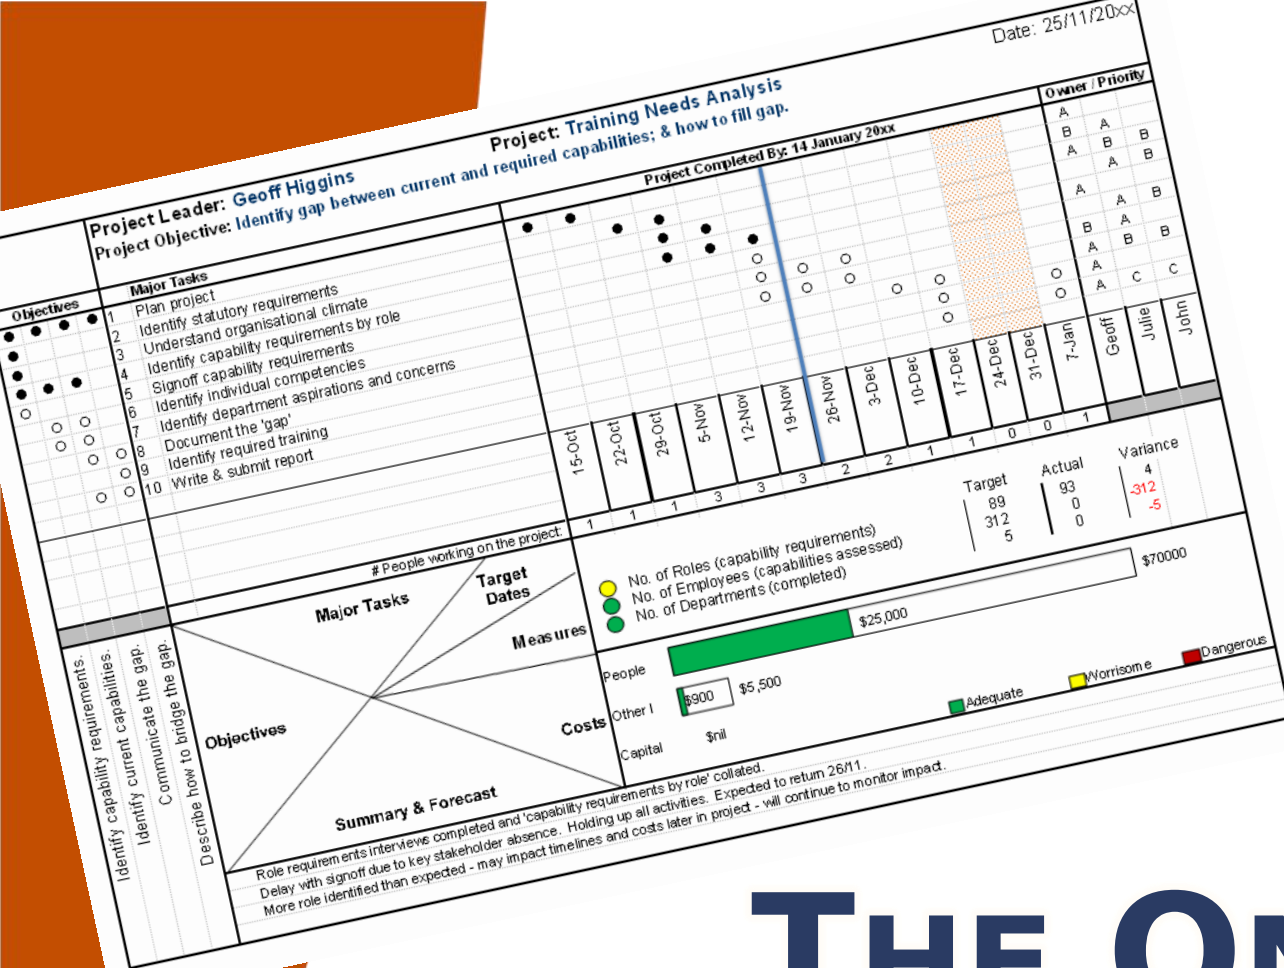

# THE ONE PAGE PROJECT MANAGER™



# **One Page Project Manager**

---

- A tool, not a methodology
- The discipline:  
To present summary project information on a single A4 sheet
- The purpose:  
To communicate the plan & progress
- Not 'simple', but reasonably straightforward

# Special Note

---

The OPPM does not take the place of other, more detailed project documentation.

Including:

- Business Case
- Project Schedule
- Risk & Issue Register
- Timesheets

# PLANNING

# General Principles

---

- Always work on the OPPM with the team/team leaders
- Get task owner agreement to commitments in the OPPM

**Project Leader: Geoff Higgins** **Project: Training Needs Analysis** **Date: 12/10/20xx**

**Project Objective: Identify gap between current and required capabilities; & how to fill gap.**

| Major Tasks                                                 | Project Completed By: 14 January 20xx |  |  |  |  |  |  |  |  |  |  |  | Owner / Priority |   |   |
|-------------------------------------------------------------|---------------------------------------|--|--|--|--|--|--|--|--|--|--|--|------------------|---|---|
| 1 Plan project                                              |                                       |  |  |  |  |  |  |  |  |  |  |  | A                |   |   |
| 2 Identify statutory requirements                           |                                       |  |  |  |  |  |  |  |  |  |  |  | B                | A |   |
| 3 Understand organisational climate                         |                                       |  |  |  |  |  |  |  |  |  |  |  | A                | B | B |
| 4 Identify capability requirements by role                  |                                       |  |  |  |  |  |  |  |  |  |  |  | A                | A | B |
| 5 Identify capability requirements by individual competence |                                       |  |  |  |  |  |  |  |  |  |  |  | B                | A | B |
| 6 Identify department aspirations                           |                                       |  |  |  |  |  |  |  |  |  |  |  | A                | B | B |
| 7 Document the 'gap'                                        |                                       |  |  |  |  |  |  |  |  |  |  |  | A                | B | B |
| 8 Identify required training                                |                                       |  |  |  |  |  |  |  |  |  |  |  | A                | C | C |
| 9 Write & submit report                                     |                                       |  |  |  |  |  |  |  |  |  |  |  |                  |   |   |

**Summary & Forecast**

| Measures                                 | Target | Actual | Variance |
|------------------------------------------|--------|--------|----------|
| No. of Roles (capability requirements)   | 89     | 0      | -89      |
| No. of Employees (capabilities assessed) | 312    | 0      | -312     |
| No. of Departments (completed)           | 5      | 0      | -5       |

**Costs**

|           |         |         |
|-----------|---------|---------|
| People    |         | \$70000 |
| Other Exp | \$5,500 |         |
| Capital   | \$nil   |         |

**Legend:** ■ Adequate ■ Worrisome ■ Dangerous

6. Link tasks with sub-objectives (using dots).
7. Create a timeline.
8. Link tasks with time (using dots).
9. Link tasks with owners (using ABC priorities).
- 9a. Add a 'people count' (optional).
10. Add quantitative or qualitative measures.
11. Add project budget.

# 0. Bring the team/team leaders together.



('Meeting Outside' c/o [www.cexp.com/officenow](http://www.cexp.com/officenow))



('All Hands Meeting' c/o [www.handsonusa.org](http://www.handsonusa.org))

Get the leaders,  
the thought leaders and  
the doers (Task Owners)  
together!



# 1. Add header details.

**Project Leader: Geoff Higgins**

**Project: Training Needs Analysis**

**Date: 12/10/20xx**


**Project Objective: Identify gap between current and required capabilities; & how to fill gap.**

## 2. Fill in task owners.

|       |       |      |
|-------|-------|------|
| Geoff | Julie | John |
|-------|-------|------|


‘Task owners’ are the workers!

### 3. Check the 'matrix'.

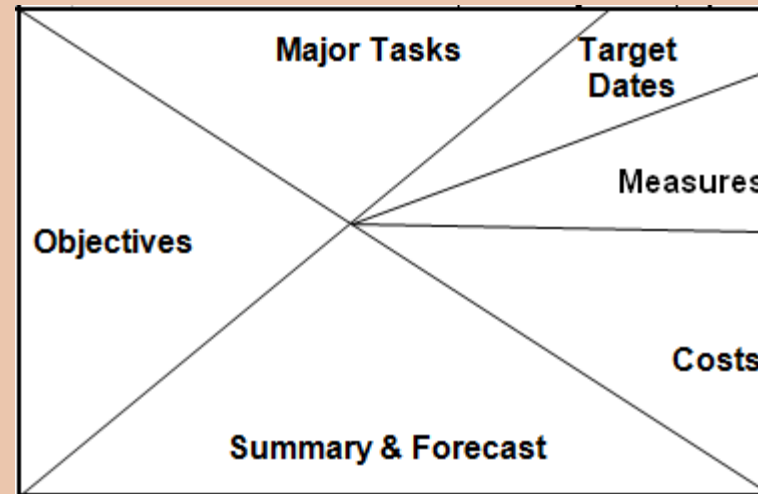

This is about not making assumptions!

#### 4. Add 3-4 sub-objectives.

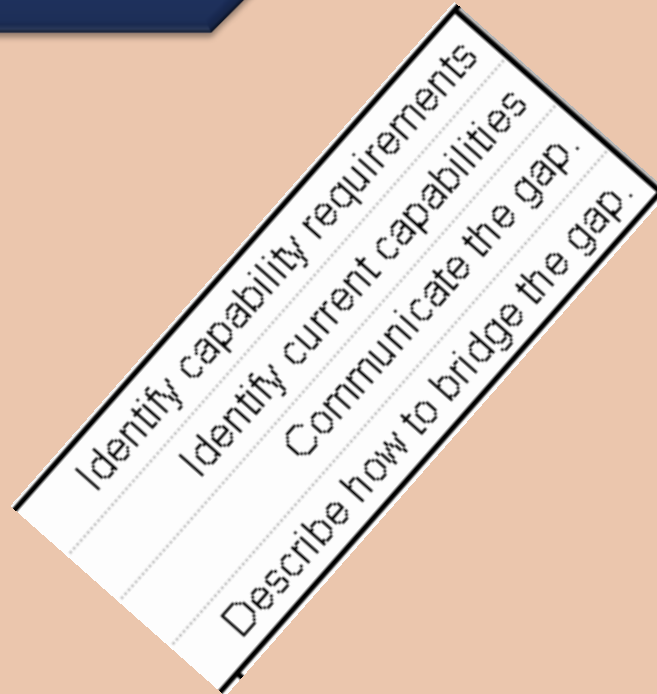

Discriminate by 'importance'!

## 5. Name the major project tasks.

| Major Tasks |                                              |
|-------------|----------------------------------------------|
| 1           | Plan project                                 |
| 2           | Identify statutory requirements              |
| 3           | Understand organisational climate            |
| 4           | Identify capability requirements by role     |
| 5           | Signoff capability requirements              |
| 6           | Identify individual competencies             |
| 7           | Identify department aspirations and concerns |
| 8           | Document the 'gap'                           |
| 9           | Identify required training                   |
| 10          | Write & submit report                        |

Again, discriminate by 'importance'!

## 6. Link tasks with sub-objectives (using dots).

| Objectives |   |   |   | Major Tasks                                    |
|------------|---|---|---|------------------------------------------------|
| ○          | ○ | ○ | ○ | 1 Plan project                                 |
| ○          |   |   |   | 2 Identify statutory requirements              |
| ○          |   |   |   | 3 Understand organisational climate            |
| ○          | ○ | ○ |   | 4 Identify capability requirements by role     |
| ○          |   |   |   | 5 Signoff capability requirements              |
|            | ○ | ○ |   | 6 Identify individual competencies             |
|            | ○ | ○ |   | 7 Identify department aspirations and concerns |
|            |   | ○ | ○ | 8 Document the 'gap'                           |
|            |   |   | ○ | 9 Identify required training                   |
|            |   | ○ | ○ | 10 Write & submit report                       |

Identify capability requirements  
 Identify current capabilities  
 Communicate the gap.  
 Describe how to bridge the gap.

Can't make a link?  
 Throw something out!



## 7. Create a timeline.

|        |        |        |       |        |        |        |       |        |        |        |        |       |
|--------|--------|--------|-------|--------|--------|--------|-------|--------|--------|--------|--------|-------|
| 15-Oct | 22-Oct | 29-Oct | 5-Nov | 12-Nov | 19-Nov | 26-Nov | 3-Dec | 10-Dec | 17-Dec | 24-Dec | 31-Dec | 7-Jan |
|--------|--------|--------|-------|--------|--------|--------|-------|--------|--------|--------|--------|-------|

Days, weeks, fortnights, months, quarters?

## 8. Link tasks with time (using dots).

| Major Tasks                                    | Project Completed By: 14 January 20xx |        |        |       |        |        |        |       |        |        |        |        |       |
|------------------------------------------------|---------------------------------------|--------|--------|-------|--------|--------|--------|-------|--------|--------|--------|--------|-------|
| 1 Plan project                                 | o                                     | o      |        |       |        |        |        |       |        |        |        |        |       |
| 2 Identify statutory requirements              |                                       |        | o      | o     |        |        |        |       |        |        |        |        |       |
| 3 Understand organisational climate            |                                       |        |        | o     | o      |        |        |       |        |        |        |        |       |
| 4 Identify capability requirements by role     |                                       |        |        | o     | o      | o      |        |       |        |        |        |        |       |
| 5 Signoff capability requirements              |                                       |        |        |       |        | o      |        |       |        |        |        |        |       |
| 6 Identify individual competencies             |                                       |        |        |       |        | o      | o      | o     |        |        |        |        |       |
| 7 Identify department aspirations and concerns |                                       |        |        |       |        | o      | o      | o     |        |        |        |        |       |
| 8 Document the 'gap'                           |                                       |        |        |       |        |        |        |       | o      | o      |        |        |       |
| 9 Identify required training                   |                                       |        |        |       |        |        |        |       |        | o      | o      |        |       |
| 10 Write & submit report                       |                                       |        |        |       |        |        |        |       |        | o      |        |        | o     |
|                                                | 15-Oct                                | 22-Oct | 29-Oct | 5-Nov | 12-Nov | 19-Nov | 26-Nov | 3-Dec | 10-Dec | 17-Dec | 24-Dec | 31-Dec | 7-Jan |

This is rough, and thus a great way to keep it simple!

## 9. Link tasks with owners (using ABC priorities).

|                               | Project Completed By: 14 January 20xx |        |        |       |        |        |        |       |        |        |        |        |       | Owner / Priority |       |      |
|-------------------------------|---------------------------------------|--------|--------|-------|--------|--------|--------|-------|--------|--------|--------|--------|-------|------------------|-------|------|
|                               | ○                                     | ○      |        |       |        |        |        |       |        |        |        |        |       | A                |       |      |
| y requirements                |                                       |        | ○      | ○     |        |        |        |       |        |        |        |        |       | B                | A     |      |
| organisational climate        |                                       |        |        | ○     | ○      |        |        |       |        |        |        |        |       | A                | B     | B    |
| ity requirements by role      |                                       |        |        | ○     | ○      | ○      |        |       |        |        |        |        |       |                  | A     | B    |
| ity requirements              |                                       |        |        |       |        | ○      |        |       |        |        |        |        |       | A                |       |      |
| al competencies               |                                       |        |        |       |        | ○      | ○      | ○     |        |        |        |        |       |                  | A     | B    |
| ment aspirations and concerns |                                       |        |        |       |        | ○      | ○      | ○     |        |        |        |        |       | B                | A     |      |
| 'gap'                         |                                       |        |        |       |        |        |        |       | ○      | ○      |        |        |       | A                | B     | B    |
| d training                    |                                       |        |        |       |        |        |        |       |        | ○      |        |        | ○     | A                |       |      |
| r report                      |                                       |        |        |       |        |        |        |       |        | ○      |        |        | ○     | A                | C     | C    |
|                               | 15-Oct                                | 22-Oct | 29-Oct | 5-Nov | 12-Nov | 19-Nov | 26-Nov | 3-Dec | 10-Dec | 17-Dec | 24-Dec | 31-Dec | 7-Jan | Geoff            | Julie | John |

Try to have a single A owner; use dots on simple projects!

## 9a. Add a 'people count' (optional).

|                                  | 15-Oct | 22-Oct | 29-Oct | 5-Nov | 12-Nov | 19-Nov | 26-Nov | 3-Dec | 10-Dec | 17-Dec | 24-Dec | 31-Dec | 7-Jan |
|----------------------------------|--------|--------|--------|-------|--------|--------|--------|-------|--------|--------|--------|--------|-------|
| # People working on the project: | 1      | 1      | 1      | 3     | 3      | 3      | 2      | 2     | 1      | 1      | 0      | 0      | 1     |

Only do this if it is useful!

## 10. Add quantitative or qualitative measures.

|                                            | Target | Actual | Variance |
|--------------------------------------------|--------|--------|----------|
| ● No. of Roles (capability requirements)   | 89     | 0      | -89      |
| ● No. of Employees (capabilities assessed) | 312    | 0      | -312     |
| ● No. of Departments (completed)           | 5      | 0      | -5       |

Use measures that are meaningful to the client!

## 11. Add project budget.

|           |                      |         |
|-----------|----------------------|---------|
| People    | <input type="text"/> | \$70000 |
| Other Exp | <input type="text"/> | \$5,500 |
| Capital   | \$nil                |         |

☒ Adequate    ☐ Worrisome    ☐ Dangerous

Ensure that the empty bars are of roughly proportional length.  
(The colour codes are for later.)

# Flexibility

---

- Don't be afraid to make changes – continuous improvement is about taking advantage of opportunities and overcoming obstacles.

When this happens, and it impacts the OPPM, change it!



# HAVE A GO YOURSELF!!!

To Download the Excel File, :  
one page project manager resources  
& download OPPM Template

| Objectives                       | Major Tasks                                    | Project Completed By: 14 January 20xx |                       |                       |                       |                       |                       |                       |                       |                       |                       |                       |                       |                       | Owner / Priority |       |      |
|----------------------------------|------------------------------------------------|---------------------------------------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|-----------------------|------------------|-------|------|
| <input type="radio"/>            | 1 Plan project                                 | <input type="radio"/>                 | <input type="radio"/> |                       |                       |                       |                       |                       |                       |                       |                       |                       |                       |                       | A                |       |      |
| <input type="radio"/>            | 2 Identify statutory requirements              |                                       |                       | <input type="radio"/> | <input type="radio"/> |                       |                       |                       |                       |                       |                       |                       |                       |                       | B                | A     |      |
| <input type="radio"/>            | 3 Understand organisational climate            |                                       |                       |                       | <input type="radio"/> | <input type="radio"/> |                       |                       |                       |                       |                       |                       |                       |                       | A                | B     | B    |
| <input type="radio"/>            | 4 Identify capability requirements by role     |                                       |                       |                       | <input type="radio"/> | <input type="radio"/> | <input type="radio"/> |                       |                       |                       |                       |                       |                       |                       |                  | A     | B    |
| <input type="radio"/>            | 5 Signoff capability requirements              |                                       |                       |                       |                       |                       | <input type="radio"/> |                       |                       |                       |                       |                       |                       |                       | A                |       |      |
| <input type="radio"/>            | 6 Identify individual competencies             |                                       |                       |                       |                       |                       | <input type="radio"/> | <input type="radio"/> | <input type="radio"/> |                       |                       |                       |                       |                       |                  | A     | B    |
| <input type="radio"/>            | 7 Identify department aspirations and concerns |                                       |                       |                       |                       |                       | <input type="radio"/> | <input type="radio"/> | <input type="radio"/> |                       |                       |                       |                       |                       | B                | A     | B    |
| <input type="radio"/>            | 8 Document the 'gap'                           |                                       |                       |                       |                       |                       |                       |                       |                       | <input type="radio"/> | <input type="radio"/> |                       |                       |                       | A                | B     | B    |
| <input type="radio"/>            | 9 Identify required training                   |                                       |                       |                       |                       |                       |                       |                       |                       |                       | <input type="radio"/> | <input type="radio"/> |                       | <input type="radio"/> | A                |       |      |
| <input type="radio"/>            | 10 Write & submit report                       |                                       |                       |                       |                       |                       |                       |                       |                       |                       |                       | <input type="radio"/> | <input type="radio"/> | <input type="radio"/> | A                | C     | C    |
|                                  |                                                | 15-Oct                                | 22-Oct                | 29-Oct                | 5-Nov                 | 12-Nov                | 19-Nov                | 26-Nov                | 3-Dec                 | 10-Dec                | 17-Dec                | 24-Dec                | 31-Dec                | 7-Jan                 | Geoff            | Julie | John |
| # People working on the project: |                                                | 1                                     | 1                     | 1                     | 3                     | 3                     | 3                     | 2                     | 2                     | 1                     | 1                     | 0                     | 0                     | 1                     |                  |       |      |

Identify capability requirements.  
Identify current capabilities.  
Communicate the gap.  
Describe how to bridge the gap.

Major Tasks
Target Dates
Measures
Objectives
Costs
Summary & Forecast

No. of Roles (capability requirements)  
No. of Employees (capabilities assessed)  
No. of Departments (completed)

Target  
89  
312  
5

Actual  
0  
0  
0

Variance  
-89  
-312  
-5

People  
Other Exp  
Capital

\$5,500

\$nil

\$70000

Adequate
Worrisome
Dangerous

Sample Project Plan – Showing the Project Plan

# MONITORING & REPORTING

# General Principles

---

- Always work on the OPPM with the team/team leaders
- Get task owner agreement to changes to commitments in the OPPM
- This is the time to identify and discuss issues and opportunities
- Do a 'Save As...' before making changes!

## Update Details

|                                                                                  |                                                                                                                                                                                                                                                                                                                       |                                  |          |
|----------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------|----------|
| Project Leader: Geoff Higgins                                                    |                                                                                                                                                                                                                                                                                                                       | Project: Training Needs Analysis |          |
| Project Objective: Identify gap between current and required capabilities; & how |                                                                                                                                                                                                                                                                                                                       |                                  |          |
| Objectives                                                                       | Major Tasks                                                                                                                                                                                                                                                                                                           | Project Completed By: 14 Jan     |          |
| ● ● ●                                                                            | 1 Plan project                                                                                                                                                                                                                                                                                                        | ● ●                              |          |
|                                                                                  | 2 Identify statutory requirements                                                                                                                                                                                                                                                                                     |                                  |          |
|                                                                                  | 3 Understand organisational climate                                                                                                                                                                                                                                                                                   | ● ● ●                            |          |
| ● ●                                                                              | 4 Identify capability requirements by role                                                                                                                                                                                                                                                                            | ● ●                              |          |
|                                                                                  | 5 Signoff capability requirements                                                                                                                                                                                                                                                                                     |                                  | ●        |
| ○ ○                                                                              | 6 Identify individual competencies                                                                                                                                                                                                                                                                                    |                                  | ○ ○ ○    |
| ○ ○                                                                              | 7 Identify department aspirations and concerns                                                                                                                                                                                                                                                                        |                                  | ○ ○ ○    |
| ○ ○                                                                              | 8 Document the 'gap'                                                                                                                                                                                                                                                                                                  |                                  |          |
| ○ ○                                                                              | 9 Identify required training                                                                                                                                                                                                                                                                                          |                                  |          |
| ○ ○                                                                              | 10 Write & submit report                                                                                                                                                                                                                                                                                              |                                  |          |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       | 15-Oct                           | 22-Oct   |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       | 29-Oct                           | 5-Nov    |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       | 12-Nov                           | 19-Nov   |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       | 26-Nov                           | 3-Dec    |
|                                                                                  | # People working on the project:                                                                                                                                                                                                                                                                                      | 1                                | 1        |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       | 1                                | 3        |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       | 3                                | 3        |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       | 3                                | 2        |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       | 2                                | 2        |
| Objectives                                                                       | Major Tasks                                                                                                                                                                                                                                                                                                           | Target Dates                     | Measures |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       |                                  |          |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       |                                  |          |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       |                                  |          |
|                                                                                  |                                                                                                                                                                                                                                                                                                                       |                                  |          |
| Objectives                                                                       | Costs                                                                                                                                                                                                                                                                                                                 | Summary & Forecast               |          |
|                                                                                  | People                                                                                                                                                                                                                                                                                                                | \$25,000                         |          |
|                                                                                  | Other                                                                                                                                                                                                                                                                                                                 | \$900 \$5,500                    |          |
|                                                                                  | Capital                                                                                                                                                                                                                                                                                                               | \$nil                            |          |
| 5                                                                                | Role requirements interviews completed and 'capability requirements by role' collated.<br>Delay with signoff due to key stakeholder absence. Holding up all activities. Expected to return 26/11.<br>More role identified than expected - may impact timelines and costs later in project - will continue to monitor. |                                  |          |

0. Bring the team/team leaders together.
1. Shift 'current date' line to the right.
2. Fill in progress dots.
3. Update product progress.
4. Update costs.
5. Fill in 'summary & forecast'.

# 0. Bring the team/team leaders together.



('All Hands Meeting' c/o [www.handsonusa.org](http://www.handsonusa.org))



('Meeting Outside' c/o [www.cexp.com/officenow](http://www.cexp.com/officenow))


Every single time!

1. Shift 'current date' line to the right.

| Project Completed By: 14 Janu |        |        |        |       |
|-------------------------------|--------|--------|--------|-------|
| ●                             |        |        |        |       |
| ●                             | ●      |        |        |       |
| ●                             | ●      | ●      |        |       |
|                               |        | ○      |        |       |
|                               |        | ○      | ○      | ○     |
|                               |        | ○      | ○      | ○     |
|                               |        |        |        |       |
|                               |        |        |        |       |
|                               |        |        |        |       |
| 5-Nov                         | 12-Nov | 19-Nov | 26-Nov | 3-Dec |



2a. Fill in progress dots.

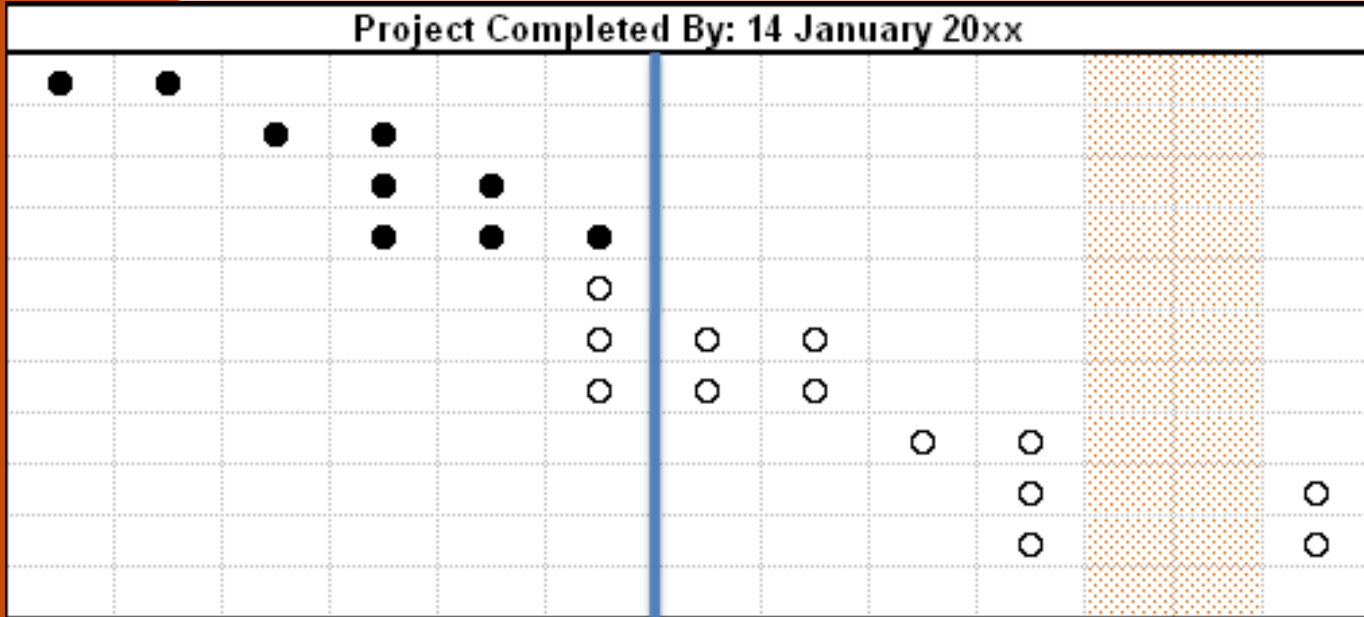

**NOT PRINTED:**


|             |      |      |      |      |
|-------------|------|------|------|------|
| Alt +       | 0152 | 0153 | 0162 | 0163 |
| Wingdings 2 | ●    | ○    | ■    | □    |

Alt + 0152 0153 0162 0163

|             |   |   |   |   |
|-------------|---|---|---|---|
| Wingdings 2 | ● | ○ | ■ | □ |
|-------------|---|---|---|---|



## 2a. Fill in progress dots.

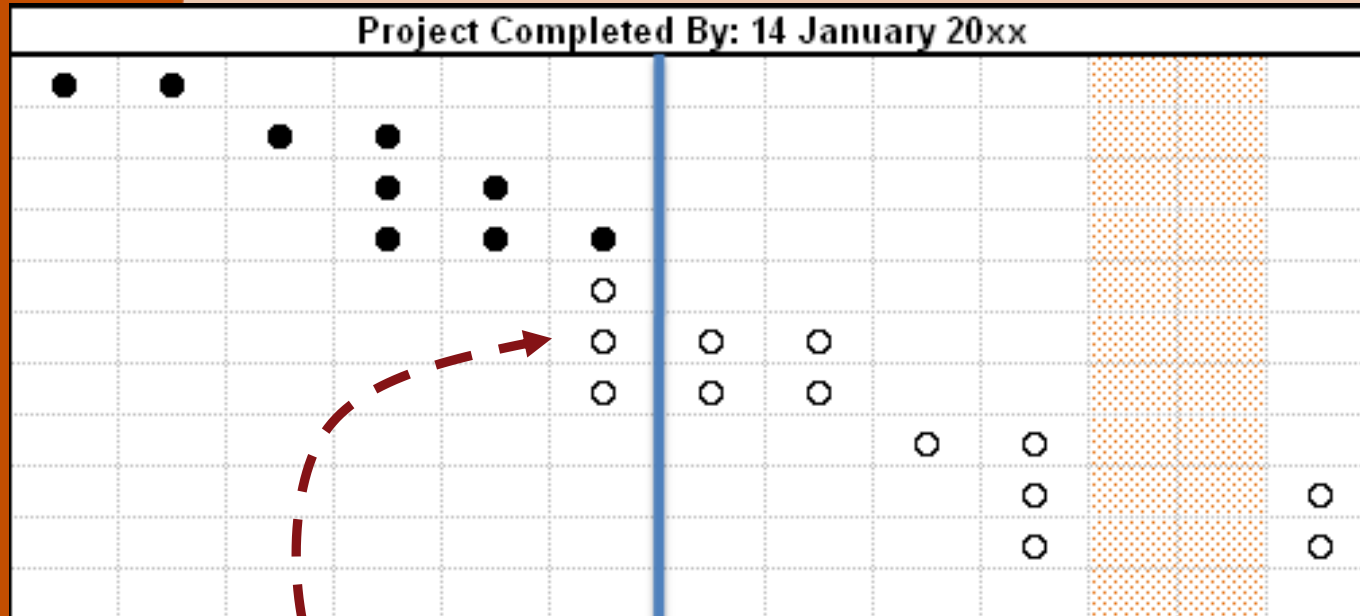

Filled in dots mean **progress**

Empty to left = 'fallen behind'

Filled to right = 'ahead of plan'

2b. Fill in **more** progress dots.

|                                  | <b>Objectives</b> |   |   |   |   |   |   |   |
|----------------------------------|-------------------|---|---|---|---|---|---|---|
| Identify capability requirements | ●                 | ● | ● | ● | ○ |   |   |   |
| Identify current capabilities    | ●                 |   | ● |   | ○ |   |   |   |
| Communicate the gap.             | ●                 |   | ● |   | ○ | ○ | ○ |   |
| Describe how to bridge the gap.  | ●                 |   |   |   |   | ○ | ○ | ○ |

### 3. Update product progress.

|                                                                                                                            | Target | Actual | Variance |
|----------------------------------------------------------------------------------------------------------------------------|--------|--------|----------|
|  No. of Roles (capability requirements)   | 89     | 93     | 4        |
|  No. of Employees (capabilities assessed) | 312    | 0      | -312     |
|  No. of Departments (completed)           | 5      | 0      | -5       |

You need to decide what the colour codes mean – for example, is it about progress or confidence.

**Green**

**Yellow**

**Red**

On Time Confident we are OK

A Little Behind

Way Behind

Not so confident


Confident we are not OK

### 3. Update product progress.

|                                                                                                                            | Target | Actual | Variance |
|----------------------------------------------------------------------------------------------------------------------------|--------|--------|----------|
|  No. of Roles (capability requirements)   | 89     | 93     | 4        |
|  No. of Employees (capabilities assessed) | 312    | 0      | -312     |
|  No. of Departments (completed)           | 5      | 0      | -5       |

Be really honest – as you cannot ‘take away’ progress in a subsequent reporting period!

## 4. Update costs.

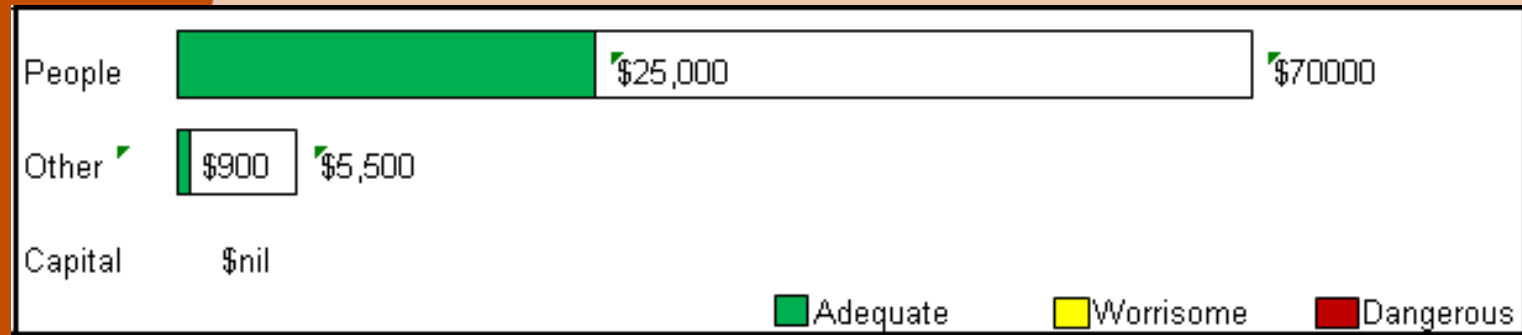

Budget colour codes are based on your forecast:

**Green**

good

(>5% below budget)

**Yellow**

not so good


(within 5% of budget)

**Red**

bad

(>5% over budget)

## 4. Update costs.

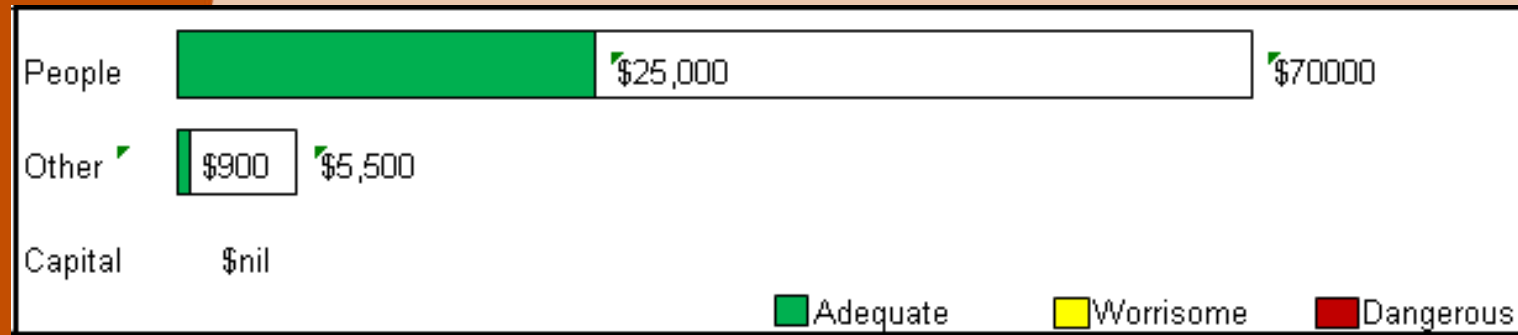

Again, be honest & accurate – as you cannot ‘take away’ progress in a subsequent reporting period!

## 5. Fill in 'summary & forecast'.

Role requirements interviews completed and 'capability requirements by role' collated.

Delay with signoff due to key stakeholder absence. Holding up all activities. Expected to return 26/11.

More role identified than expected - may impact timelines and costs later in project - will continue to monitor impact.

1. Looking back, describe 'how the project is going' in your words.
2. Looking forward, describe what is coming up.
3. Describe major milestones, risks, issues, and opportunities.
4. Explain all **red** content.

|                                                                                                                                |  |  |  |                                                                                                                            |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |
|--------------------------------------------------------------------------------------------------------------------------------|--|--|--|----------------------------------------------------------------------------------------------------------------------------|--|--|--|--|--|--|--|--|--|-----------------------------------------------------------------------------------------|--|--|--|--|--|--|--|--|--|-----------------------|--|--|-----------------------|--|--|----------|--|--|
|                                                                                                                                |  |  |  | Project Leader: Geoff Higgins                                                                                              |  |  |  |  |  |  |  |  |  | Project: Training Needs Analysis                                                        |  |  |  |  |  |  |  |  |  | Date: 25/11/20xx      |  |  |                       |  |  |          |  |  |
|                                                                                                                                |  |  |  | Project Objective: Identify gap between current and required capabilities; & how to fill gap.                              |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |
| Objectives                                                                                                                     |  |  |  | Major Tasks                                                                                                                |  |  |  |  |  |  |  |  |  | Project Completed By: 14 January 20xx                                                   |  |  |  |  |  |  |  |  |  |                       |  |  | Owner / Priority      |  |  |          |  |  |
| ● ● ● ●                                                                                                                        |  |  |  | 1 Plan project                                                                                                             |  |  |  |  |  |  |  |  |  | ● ●                                                                                     |  |  |  |  |  |  |  |  |  |                       |  |  | A                     |  |  |          |  |  |
| ●                                                                                                                              |  |  |  | 2 Identify statutory requirements                                                                                          |  |  |  |  |  |  |  |  |  | ● ●                                                                                     |  |  |  |  |  |  |  |  |  |                       |  |  | B A                   |  |  |          |  |  |
| ●                                                                                                                              |  |  |  | 3 Understand organisational climate                                                                                        |  |  |  |  |  |  |  |  |  | ● ●                                                                                     |  |  |  |  |  |  |  |  |  |                       |  |  | A B B                 |  |  |          |  |  |
| ● ● ●                                                                                                                          |  |  |  | 4 Identify capability requirements by role                                                                                 |  |  |  |  |  |  |  |  |  | ● ● ●                                                                                   |  |  |  |  |  |  |  |  |  |                       |  |  | A B                   |  |  |          |  |  |
| ○                                                                                                                              |  |  |  | 5 Signoff capability requirements                                                                                          |  |  |  |  |  |  |  |  |  | ○                                                                                       |  |  |  |  |  |  |  |  |  |                       |  |  | A                     |  |  |          |  |  |
| ○ ○                                                                                                                            |  |  |  | 6 Identify individual competencies                                                                                         |  |  |  |  |  |  |  |  |  | ○ ○ ○                                                                                   |  |  |  |  |  |  |  |  |  |                       |  |  | A B                   |  |  |          |  |  |
| ○ ○                                                                                                                            |  |  |  | 7 Identify department aspirations and concerns                                                                             |  |  |  |  |  |  |  |  |  | ○ ○ ○                                                                                   |  |  |  |  |  |  |  |  |  |                       |  |  | B A                   |  |  |          |  |  |
| ○ ○                                                                                                                            |  |  |  | 8 Document the 'gap'                                                                                                       |  |  |  |  |  |  |  |  |  | ○ ○                                                                                     |  |  |  |  |  |  |  |  |  |                       |  |  | A B B                 |  |  |          |  |  |
| ○ ○                                                                                                                            |  |  |  | 9 Identify required training                                                                                               |  |  |  |  |  |  |  |  |  | ○ ○                                                                                     |  |  |  |  |  |  |  |  |  |                       |  |  | A                     |  |  |          |  |  |
| ○ ○                                                                                                                            |  |  |  | 10 Write & submit report                                                                                                   |  |  |  |  |  |  |  |  |  | ○ ○                                                                                     |  |  |  |  |  |  |  |  |  |                       |  |  | A C C                 |  |  |          |  |  |
|                                                                                                                                |  |  |  |                                                                                                                            |  |  |  |  |  |  |  |  |  | 15-Oct 22-Oct 29-Oct 5-Nov 12-Nov 19-Nov 26-Nov 3-Dec 10-Dec 17-Dec 24-Dec 31-Dec 7-Jan |  |  |  |  |  |  |  |  |  |                       |  |  | Geoff Julie John      |  |  |          |  |  |
|                                                                                                                                |  |  |  | # People working on the project:                                                                                           |  |  |  |  |  |  |  |  |  | 1 1 1 3 3 3 2 2 1 1 0 0 1                                                               |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |
| Identify capability requirements.<br>Identify current capabilities.<br>Communicate the gap.<br>Describe how to bridge the gap. |  |  |  | <div>Major Tasks</div> <div>Target Dates</div> <div>Measures</div> <div>Objectives</div> <div>Summary &amp; Forecast</div> |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  | Target                |  |  | Actual                |  |  | Variance |  |  |
|                                                                                                                                |  |  |  |                                                                                                                            |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  | 89                    |  |  | 93                    |  |  | 4        |  |  |
|                                                                                                                                |  |  |  |                                                                                                                            |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  | 312                   |  |  | 0                     |  |  | -312     |  |  |
|                                                                                                                                |  |  |  |                                                                                                                            |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  | 5                     |  |  | 0                     |  |  | -5       |  |  |
|                                                                                                                                |  |  |  |                                                                                                                            |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |
|                                                                                                                                |  |  |  | People                                                                                                                     |  |  |  |  |  |  |  |  |  | <div></div> \$25,000                                                                    |  |  |  |  |  |  |  |  |  | \$70000               |  |  |                       |  |  |          |  |  |
|                                                                                                                                |  |  |  | Other I                                                                                                                    |  |  |  |  |  |  |  |  |  | <div></div> \$900 \$5,500                                                               |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |
|                                                                                                                                |  |  |  | Capital                                                                                                                    |  |  |  |  |  |  |  |  |  | \$nil                                                                                   |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |
|                                                                                                                                |  |  |  |                                                                                                                            |  |  |  |  |  |  |  |  |  | <div></div> Adequate                                                                    |  |  |  |  |  |  |  |  |  | <div></div> Worrisome |  |  | <div></div> Dangerous |  |  |          |  |  |
|                                                                                                                                |  |  |  | Role requirements interviews completed and 'capability requirements by role' collated.                                     |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |
|                                                                                                                                |  |  |  | Delay with signoff due to key stakeholder absence. Holding up all activities. Expected to return 26/11.                    |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |
|                                                                                                                                |  |  |  | More role identified than expected - may impact timelines and costs later in project - will continue to monitor impact.    |  |  |  |  |  |  |  |  |  |                                                                                         |  |  |  |  |  |  |  |  |  |                       |  |  |                       |  |  |          |  |  |

Sample Project Plan – Showing Project Progress



# Reading & Resources

---

- Campbell, CA 2007 *The One-Page Project Manager* Wiley & Sons, New Jersey.
- Campbell's Resources at [www.onepageprojectmanager.com/oppm/resource.html](http://www.onepageprojectmanager.com/oppm/resource.html)
- Balanced customer review on Amazon.com <http://www.amazon.com/review/R1M1BI11AF4D7N>

© Performance People Pty Ltd, 2009

The One Page Project Manager is the  
property of O.C.Tanner Co.

Photos courtesy of [www.flickr.com](http://www.flickr.com).  
(Under creative commons license.)

Added to SlideShare by  
Geoff at Performance People
